


























































































































































ID		Task Mode	WBS	Task Name	Duration	Start	Finish	Pred	11-02	
1			1	Project - Suumaya - Mobile app for Shopping	109 days	Fri 01-03-24	Wed 31-07-24			
2			1.1	Delivery of Online shopping Mobile app	66 days	Fri 01-03-24	Fri 31-05-24			
3			1.1.1	Project Management	66 days	Fri 01-03-24	Fri 31-05-24			
4			1.1.1.1	Define Project Scope	4 days	Fri 01-03-24	Wed 06-03-24			
5			1.1.1.1.1	Review Stakeholder Requirements	2 days	Fri 01-03-24	Mon 04-03-24			
6			1.1.1.1.2	Identify Project Constraints	2 days	Tue 05-03-24	Wed 06-03-24	5		
7			1.1.1.1.3	Define Project Deliverables	2 days	Tue 05-03-24	Wed 06-03-24	5		
8			1.1.1.2	Develop Project Plan	4 days	Thu 07-03-24	Tue 12-03-24			
9			1.1.1.2.1	Define Project Timeline	1 day	Thu 07-03-24	Thu 07-03-24	7		
10			1.1.1.2.2	Allocate Project Resources	1 day	Thu 07-03-24	Thu 07-03-24	7		
11			1.1.1.2.3	Review and Approval of Project Plan	3 days	Fri 08-03-24	Tue 12-03-24	10		
12			1.1.1.3	Team Kick-off and Training	11 days	Fri 08-03-24	Fri 22-03-24			
13			1.1.1.3.1	Conduct Team Introduction	1 day	Fri 08-03-24	Fri 08-03-24	10		
14			1.1.1.3.2	Provide Project Training	10 days	Mon 11-03-24	Fri 22-03-24	13		
15			1.1.1.4	Project Execution	66 days	Fri 01-03-24	Fri 31-05-24			
16			1.1.1.5	Project Monitoring & Control	66 days	Fri 01-03-24	Fri 31-05-24			
17			1.1.1.6	Risk Management	66 days	Fri 01-03-24	Fri 31-05-24			
18			1.1.2	Requirement Analysis	10 days	Wed 13-03-24	Tue 26-03-24			
19			1.1.2.1	Stakeholder Interviews	10 days	Wed 13-03-24	Tue 26-03-24			
20			1.1.2.1.1	Schedule Stakeholder Meetings	3 days	Wed 13-03-24	Fri 15-03-24	11		
21			1.1.2.1.2	Conduct Stakeholder Interviews	7 days	Mon 18-03-24	Tue 26-03-24	20		
22			1.1.2.2	Market Research	6 days	Wed 13-03-24	Wed 20-03-24			

Project: OnlineShopping\_mobil  
Date: Thu 15-02-24

























Task		Rolled Up Progress		Manual Summary Rollup	
Split		External Tasks		Manual Summary	
Milestone		External Milestone		Start-only	
Summary		Inactive Task		Finish-only	
Project Summary		Inactive Milestone		Deadline	
Group By Summary		Inactive Summary		Critical	
Rolled Up Task		Manual Task		Critical Split	
Rolled Up Milestone		Duration-only		Progress	























ID		Task Mode	WBS	Task Name	Duration	Start	Finish	Pred	11-02	
23			1.1.2.2.1	Identify Target Audience	3 days	Wed 13-03-24	Fri 15-03-24	11		
24			1.1.2.2.2	Analyze Market Trends	3 days	Mon 18-03-24	Wed 20-03-24	23		
25			<b>1.1.3</b>	<b>Design</b>	<b>35 days</b>	<b>Mon 18-03-24 Fri 03-05-24</b>				
26			<b>1.1.3.1</b>	<b>UI/UX Design</b>	<b>25 days</b>	<b>Mon 18-03-24 Fri 19-04-24</b>				
27			1.1.3.1.1	Wireframe Development	10 days	Mon 18-03-24	Fri 29-03-24	20		
28			1.1.3.1.2	Prototype Creation	15 days	Mon 01-04-24	Fri 19-04-24	27		
29			<b>1.1.3.2</b>	<b>Database Design</b>	<b>10 days</b>	<b>Mon 22-04-24 Fri 03-05-24</b>				
30			1.1.3.2.1	Database Schema Planning	5 days	Mon 22-04-24	Fri 26-04-24	28		
31			1.1.3.2.2	Data Model Implementation	5 days	Mon 29-04-24	Fri 03-05-24	30		
32			<b>1.1.4</b>	<b>Development</b>	<b>15 days</b>	<b>Mon 06-05-24 Fri 24-05-24</b>				
33			<b>1.1.4.1</b>	<b>Frontend Development (ios &amp; android)</b>	<b>9 days</b>	<b>Mon 06-05-24 Thu 16-05-24</b>				
34			1.1.4.1.1	UI Coding	4 days	Mon 06-05-24	Thu 09-05-24	31		
35			1.1.4.1.2	Responsive Design Implementation	5 days	Fri 10-05-24	Thu 16-05-24	34		
36			<b>1.1.4.2</b>	<b>Backend Development</b>	<b>6 days</b>	<b>Fri 17-05-24 Fri 24-05-24</b>				
37			1.1.4.2.1	Server Setup and Configuration	3 days	Fri 17-05-24	Tue 21-05-24	35		
38			1.1.4.2.2	API Development	3 days	Wed 22-05-24	Fri 24-05-24	37		
39			<b>1.1.5</b>	<b>Testing</b>	<b>15 days</b>	<b>Fri 10-05-24 Thu 30-05-24</b>				
40			<b>1.1.5.1</b>	<b>Unit Testing</b>	<b>5 days</b>	<b>Fri 10-05-24 Thu 16-05-24</b>				
41			1.1.5.1.1	Code Unit Testing	5 days	Fri 10-05-24	Thu 16-05-24	34		
42			1.1.5.1.2	UI Unit Testing	5 days	Fri 10-05-24	Thu 16-05-24	34		
43			<b>1.1.5.2</b>	<b>Integration Testing</b>	<b>10 days</b>	<b>Fri 17-05-24 Thu 30-05-24</b>				
44			1.1.5.2.1	API Integration Testing	4 days	Fri 17-05-24	Wed 22-05-24	40		

























Project: OnlineShopping_mobil Date: Thu 15-02-24	Task		Rolled Up Progress		Manual Summary Rollup	
	Split		External Tasks		Manual Summary	
	Milestone		External Milestone		Start-only	
	Summary		Inactive Task		Finish-only	
	Project Summary		Inactive Milestone		Deadline	
	Group By Summary		Inactive Summary		Critical	
	Rolled Up Task		Manual Task		Critical Split	
	Rolled Up Milestone		Duration-only		Progress	


ID		Task Mode	WBS	Task Name	Duration	Start	Finish	Pred	11-02	
45			1.1.5.2.2	System Integration Testing	4 days	Thu 23-05-24	Tue 28-05-24	44		
46			1.1.5.2.3	QC approval for Product release	2 days	Wed 29-05-24	Thu 30-05-24	45		
47			1.1.6	Deployment	3 days	Wed 29-05-24	Fri 31-05-24			
48			1.1.6.1	Deployment Plan	2 days	Wed 29-05-24	Thu 30-05-24			
49			1.1.6.1.1	Plan Server Configuration	1 day	Wed 29-05-24	Wed 29-05-24	45		
50			1.1.6.1.2	Implement Rollback Strategy	1 day	Thu 30-05-24	Thu 30-05-24	49		
51			1.1.6.2	Server Deployment	3 days	Wed 29-05-24	Fri 31-05-24			
52			1.1.6.2.1	Configure Hosting Environment	1 day	Wed 29-05-24	Wed 29-05-24	45		
53			1.1.6.2.2	Deploy Application	1 day	Fri 31-05-24	Fri 31-05-24	46		
54			1.1.7	Training and Documentation	11 days	Fri 17-05-24	Fri 31-05-24			
55			1.1.7.1	User Training	7 days	Fri 17-05-24	Mon 27-05-24			
56			1.1.7.1.1	Conduct User Workshops	4 days	Fri 17-05-24	Wed 22-05-24	42		
57			1.1.7.1.2	Provide Training Materials	3 days	Thu 23-05-24	Mon 27-05-24	56		
58			1.1.7.2	Technical Documentation	5 days	Mon 27-05-24	Fri 31-05-24			
59			1.1.7.2.1	Create User Manuals	5 days	Mon 27-05-24	Fri 31-05-24	32		
60			1.1.8	Project Closure	1 day	Fri 31-05-24	Fri 31-05-24			
61			1.1.8.1	Final review of deliverables	1 day	Fri 31-05-24	Fri 31-05-24	46		
62			1.1.8.2	Stakeholder approval of sign off	1 day	Fri 31-05-24	Fri 31-05-24	46		
63			1.1.8.3	Project debrief - record lessons learnt	1 day	Fri 31-05-24	Fri 31-05-24	46		
64			1.1.8.4	Storage of artifacts into repository	1 day	Fri 31-05-24	Fri 31-05-24	46		
65			1.2	Marketing and Promotion	23 days	Wed 27-03-24	Fri 26-04-24			
66			1.2.1	Marketing Strategy	13 days	Wed 27-03-24	Fri 12-04-24			

Project: OnlineShopping\_mobil  
Date: Thu 15-02-24


Task		Rolled Up Progress		Manual Summary Rollup	
Split		External Tasks		Manual Summary	
Milestone		External Milestone		Start-only	
Summary		Inactive Task		Finish-only	
Project Summary		Inactive Milestone		Deadline	
Group By Summary		Inactive Summary		Critical	
Rolled Up Task		Manual Task		Critical Split	
Rolled Up Milestone		Duration-only		Progress	





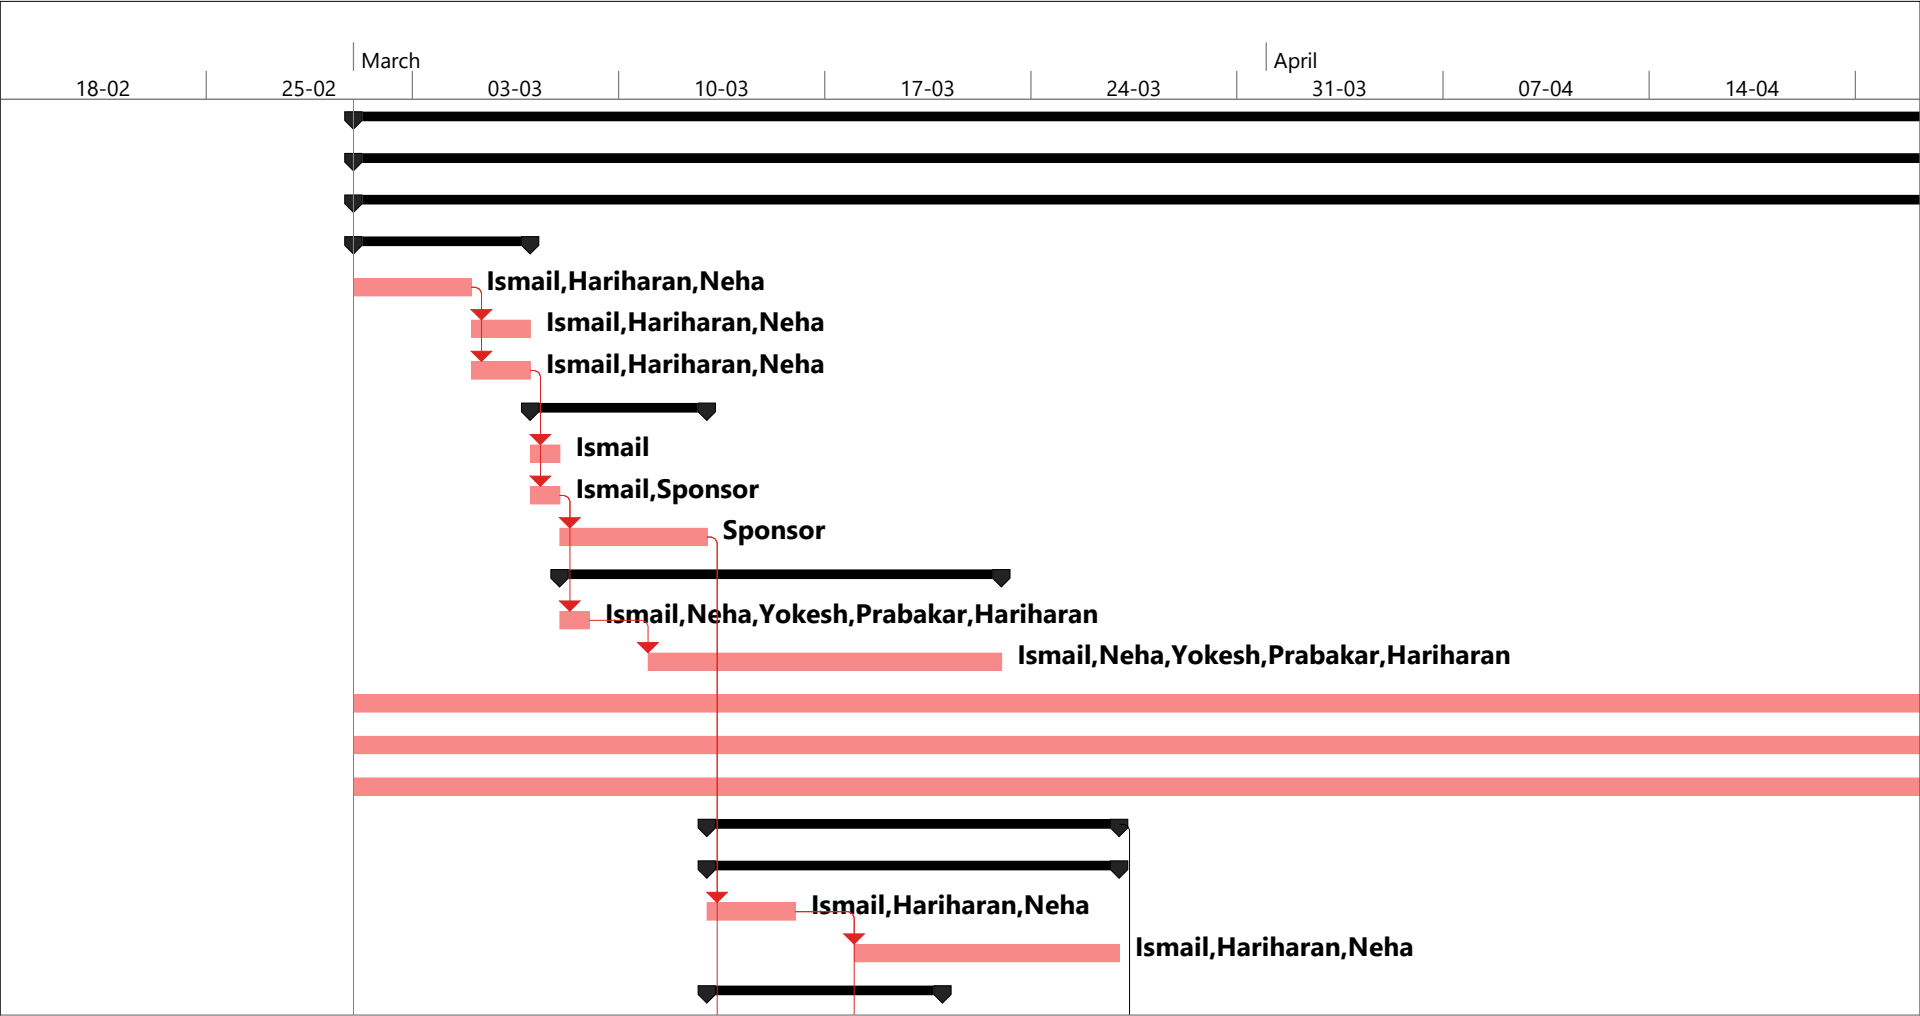



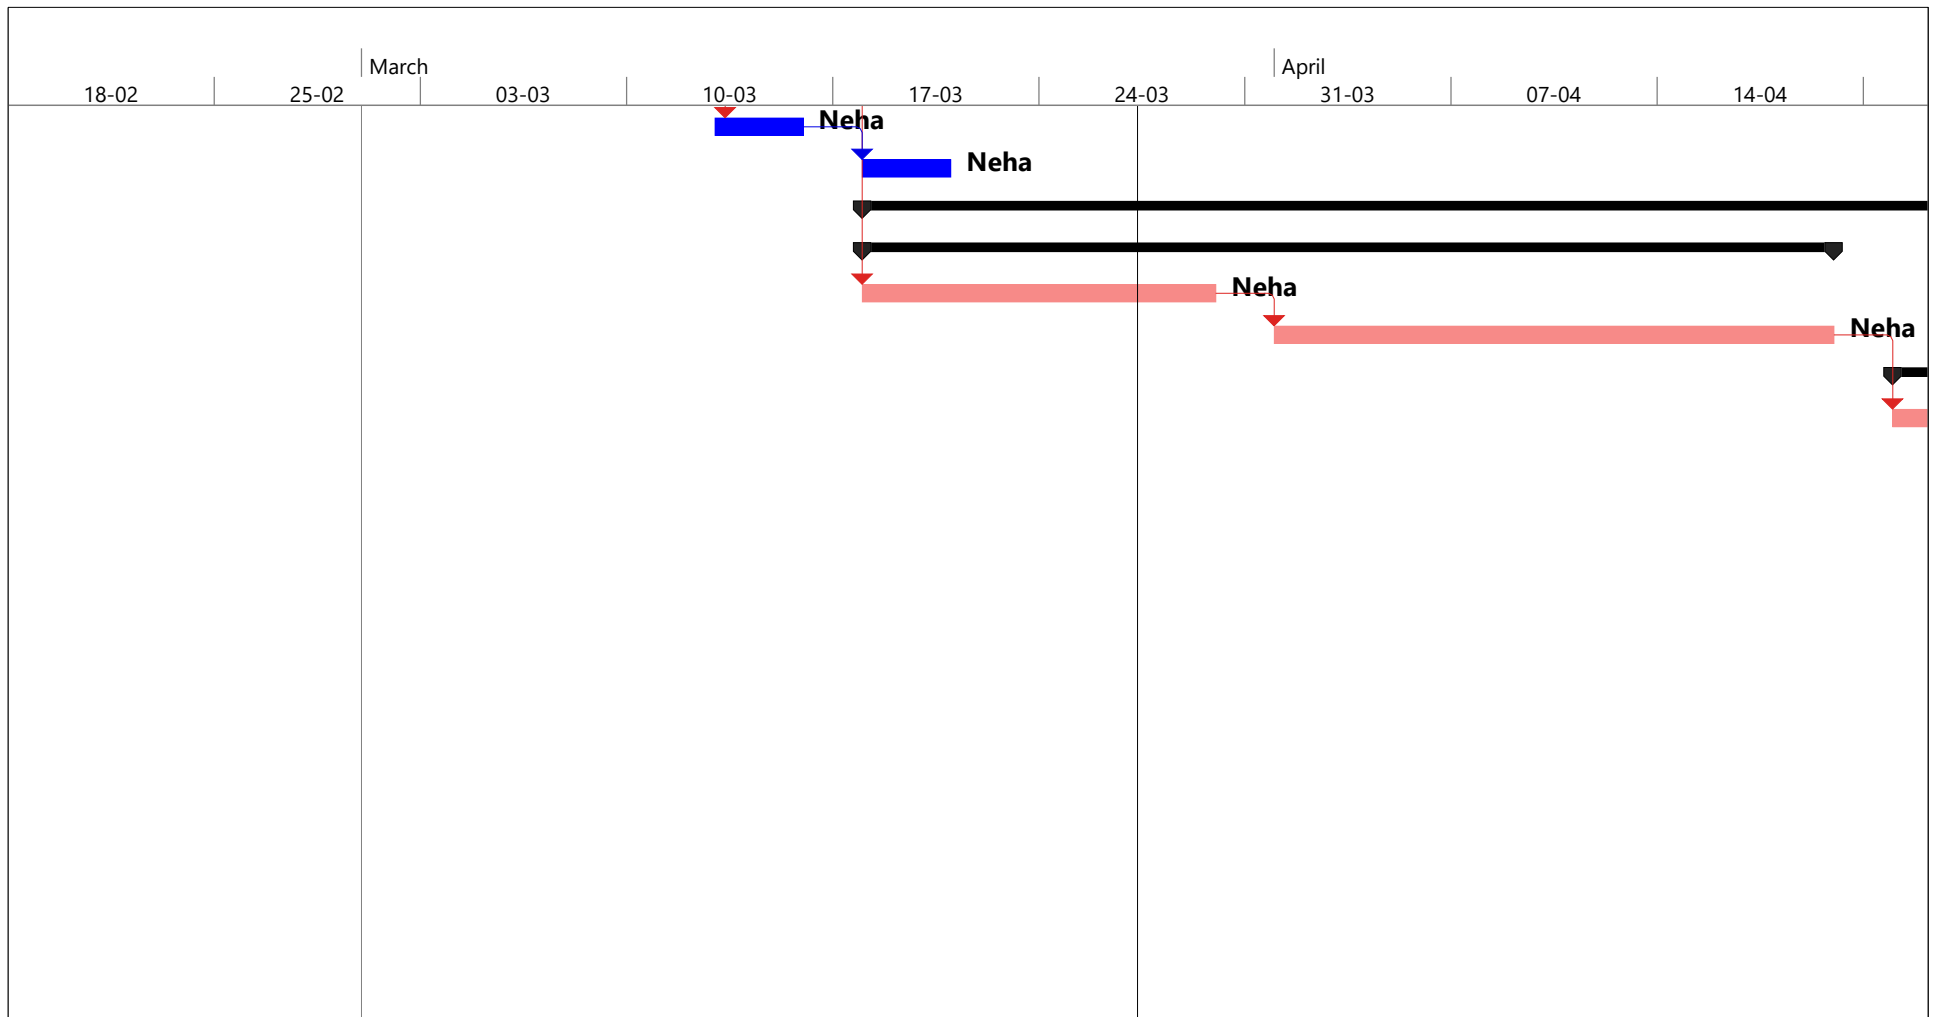















ID		Task Mode	WBS	Task Name	Duration	Start	Finish	Prede	11-02	
67			1.2.1.1	Develop Marketing Plan	3 days	Wed 27-03-2	Fri 29-03-24	18		
68			1.2.1.2	Implement Social Media Campaigns	10 days	Mon 01-04-2	Fri 12-04-24	67		
69			<b>1.2.2</b>	<b>Social Media Promotion</b>	<b>4 days</b>	<b>Mon 15-04-2 Thu 18-04-24</b>				
70			1.2.2.1	Create Engaging Content	2 days	Mon 15-04-2	Tue 16-04-24	68		
71			1.2.2.2	Schedule and Post Content	2 days	Wed 17-04-2	Thu 18-04-24	70		
72			<b>1.2.3</b>	<b>Advertising Campaigns</b>	<b>6 days</b>	<b>Fri 19-04-24 Fri 26-04-24</b>				
73			1.2.3.1	Design Advertisements	3 days	Fri 19-04-24	Tue 23-04-24	69		
74			1.2.3.2	Launch Ad Campaigns	3 days	Wed 24-04-2	Fri 26-04-24	73		
75			<b>1.3</b>	<b>Maintenance and Support</b>	<b>43 days</b>	<b>Mon 03-06-2 Wed 31-07-24</b>				
76			<b>1.3.1</b>	<b>Bug Fixes and Updates</b>	<b>43 days</b>	<b>Mon 03-06-2 Wed 31-07-24</b>				
77			1.3.1.1	Identify and Resolve Bugs	43 days	Mon 03-06-2	Wed 31-07-24			
78			1.3.1.2	Implement System Updates - Ongoing	43 days	Mon 03-06-2	Wed 31-07-24			
79			<b>1.3.2</b>	<b>Customer Support</b>	<b>30 days</b>	<b>Mon 03-06-2 Fri 12-07-24</b>				


Project: OnlineShopping_mobil Date: Thu 15-02-24	Task		Rolled Up Progress		Manual Summary Rollup	
	Split		External Tasks		Manual Summary	
	Milestone		External Milestone		Start-only	
	Summary		Inactive Task		Finish-only	
	Project Summary		Inactive Milestone		Deadline	
	Group By Summary		Inactive Summary		Critical	
	Rolled Up Task		Manual Task		Critical Split	
	Rolled Up Milestone		Duration-only		Progress	









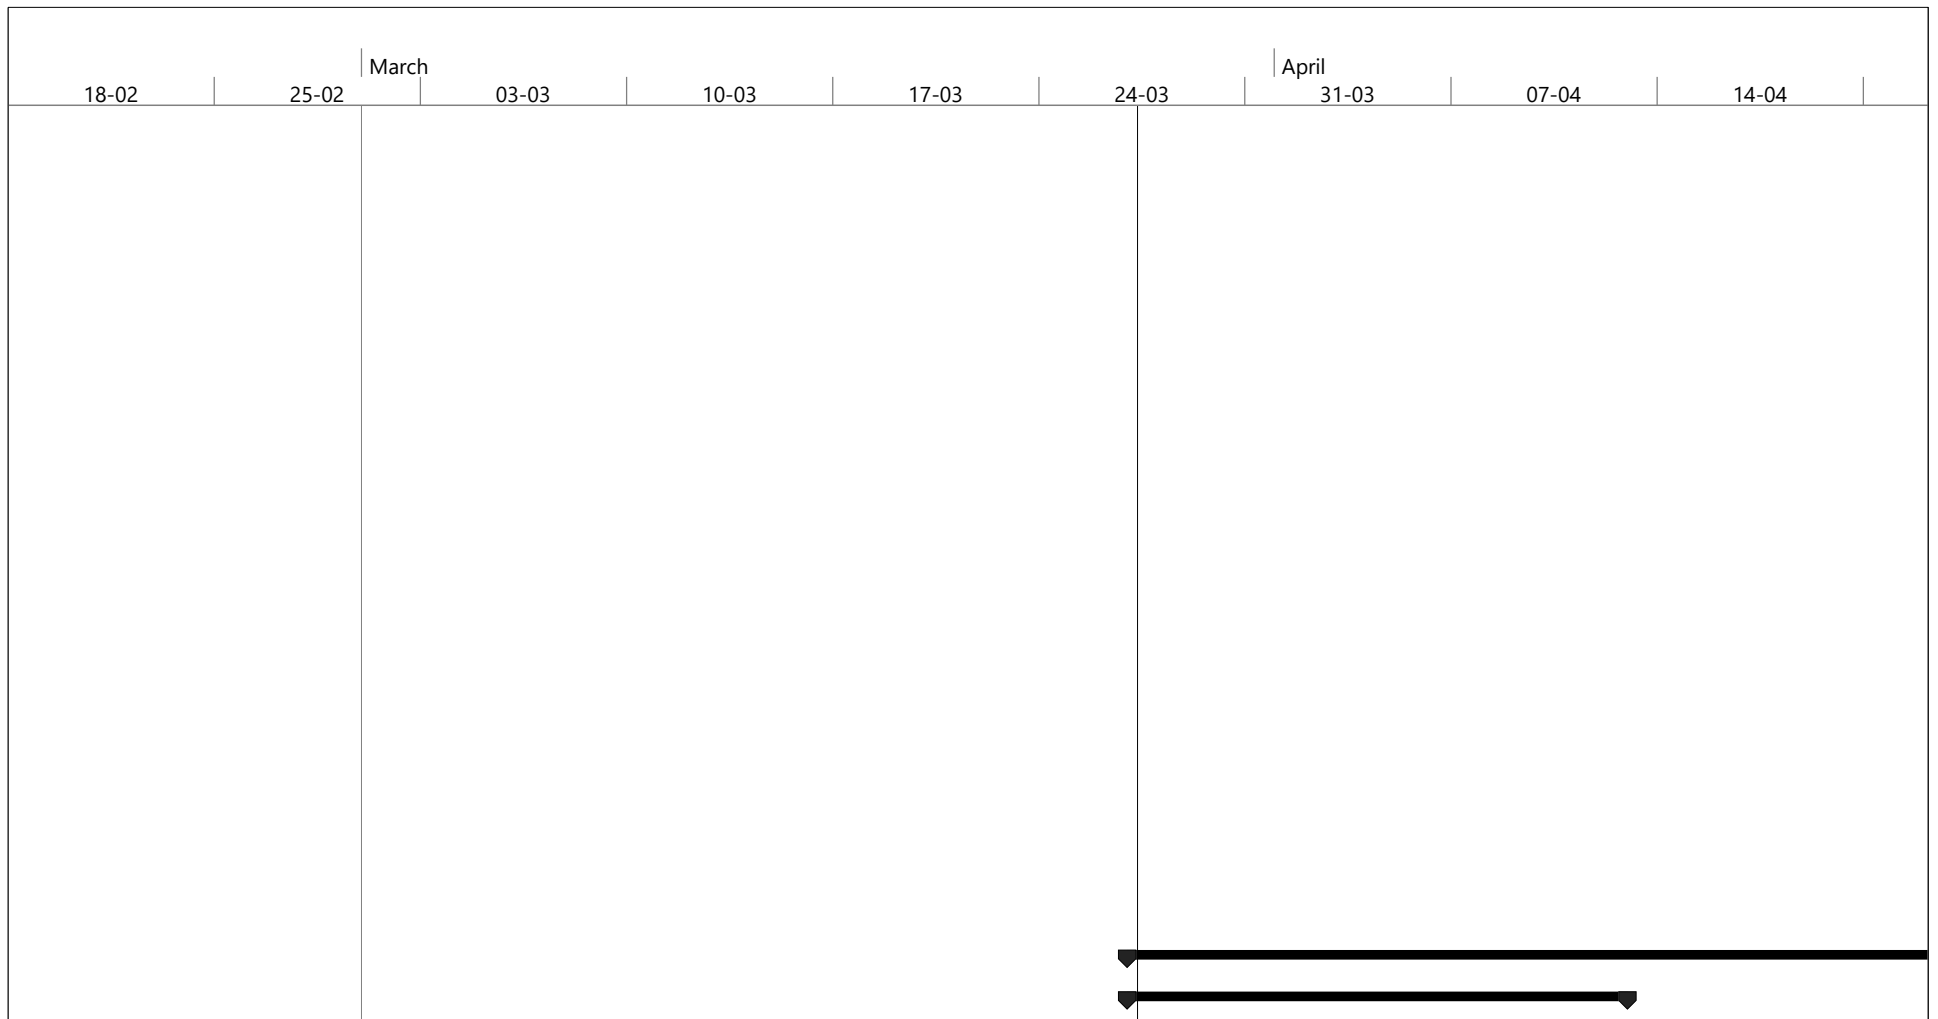








Project: OnlineShopping_mobil Date: Thu 15-02-24	Task		Rolled Up Progress		Manual Summary Rollup	
	Split		External Tasks		Manual Summary	
	Milestone		External Milestone		Start-only	
	Summary		Inactive Task		Finish-only	
	Project Summary		Inactive Milestone		Deadline	
	Group By Summary		Inactive Summary		Critical	
	Rolled Up Task		Manual Task		Critical Split	
	Rolled Up Milestone		Duration-only		Progress	



Project: OnlineShopping_mobil Date: Thu 15-02-24	Task		Rolled Up Progress		Manual Summary Rollup	
	Split		External Tasks		Manual Summary	
	Milestone		External Milestone		Start-only	
	Summary		Inactive Task		Finish-only	
	Project Summary		Inactive Milestone		Deadline	
	Group By Summary		Inactive Summary		Critical	
	Rolled Up Task		Manual Task		Critical Split	
	Rolled Up Milestone		Duration-only		Progress	



Task		Manual Summary Rollup	
Task		Rolled Up Progress	
Split		External Tasks	
Milestone		External Milestone	
Summary		Inactive Task	
Project Summary		Inactive Milestone	
Group By Summary		Inactive Summary	
Rolled Up Task		Manual Task	
Rolled Up Milestone		Duration-only	
